


Project Update – Milwaukee County Board


October 1, 2021

EAST
WEST **BRT**

The East-West Corridor

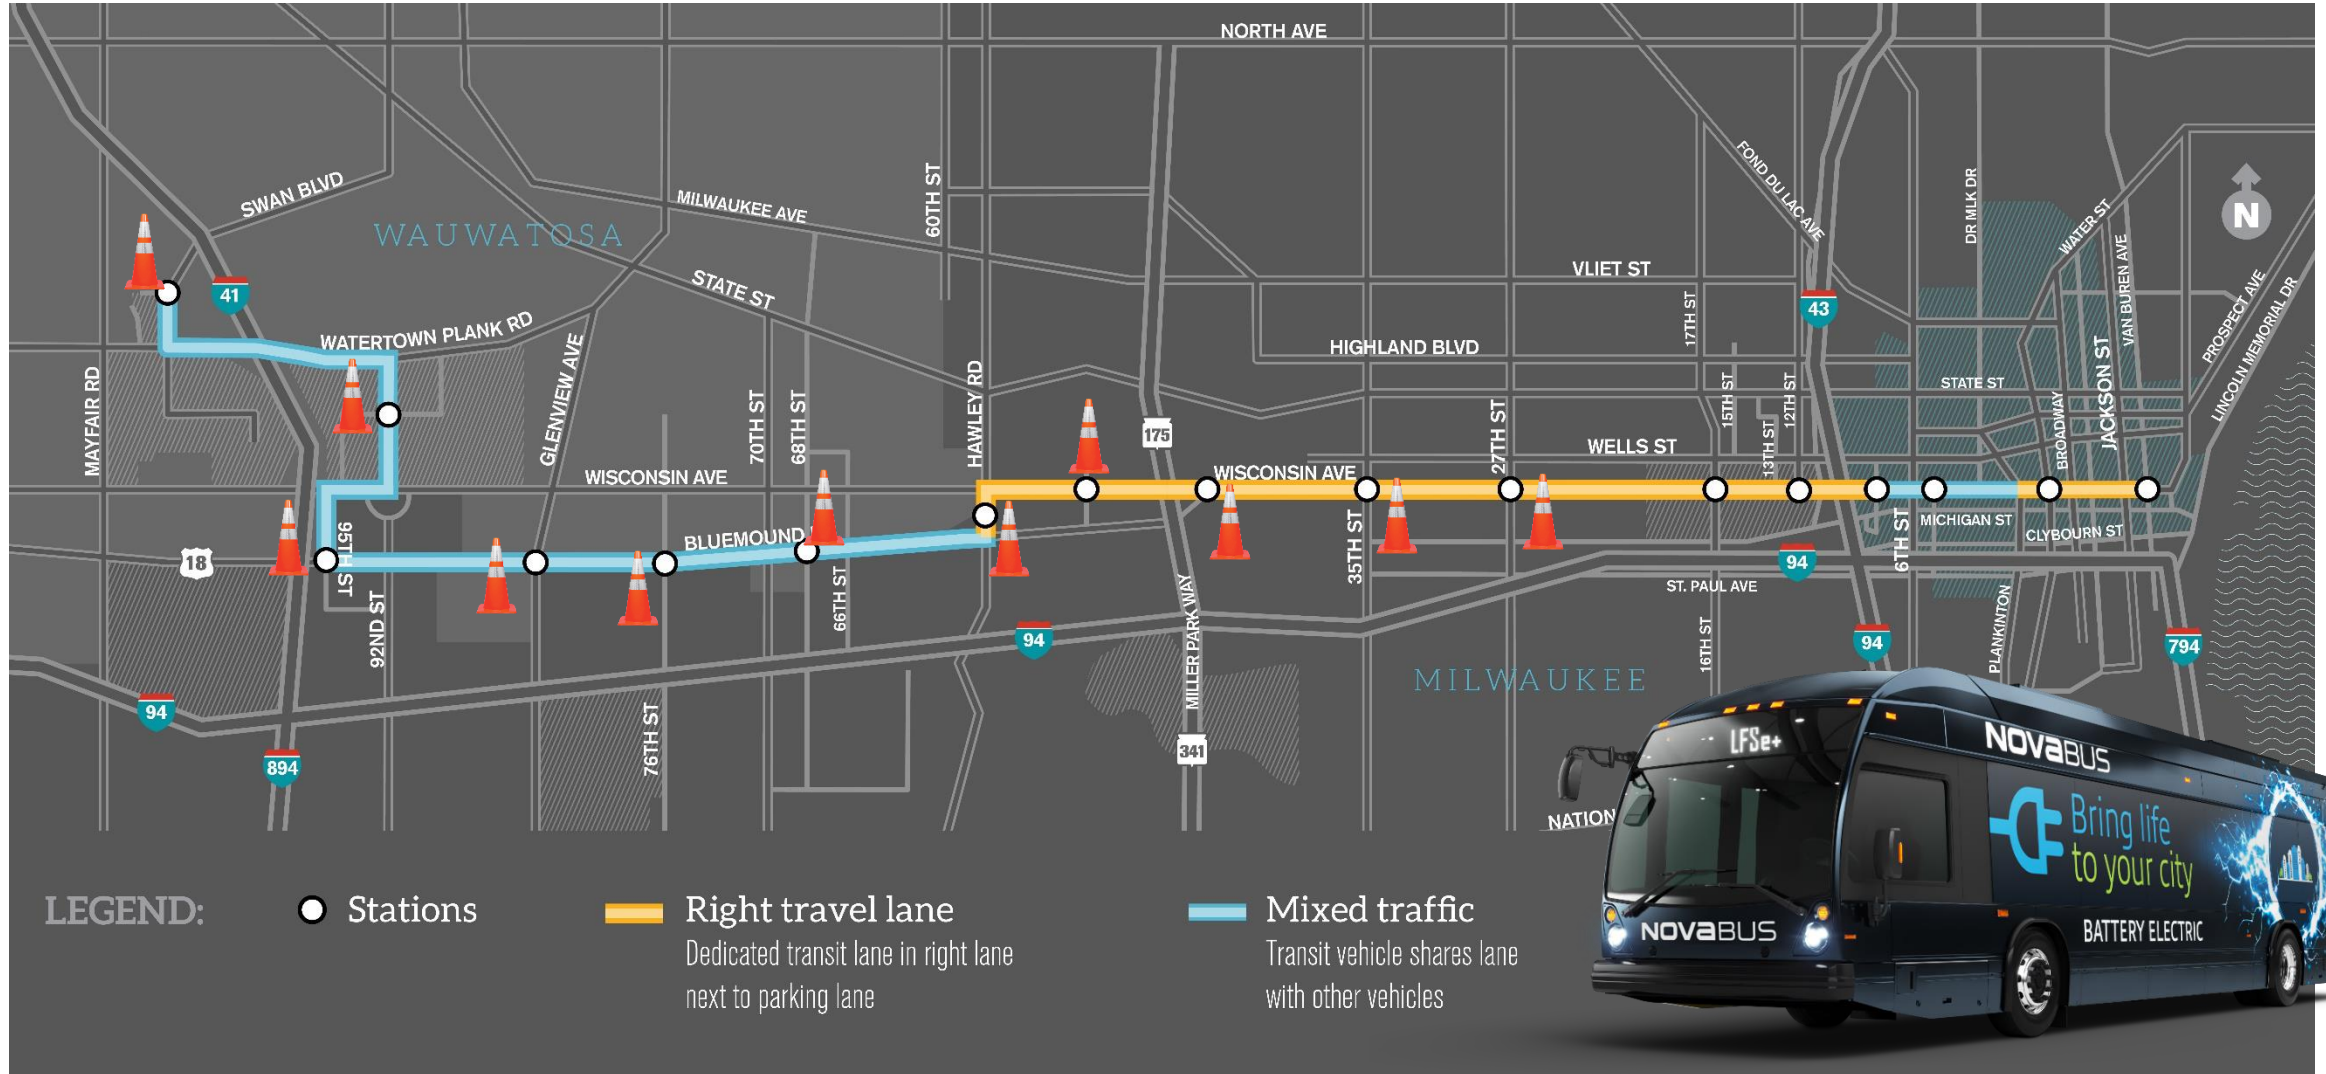

CONSTRUCTION

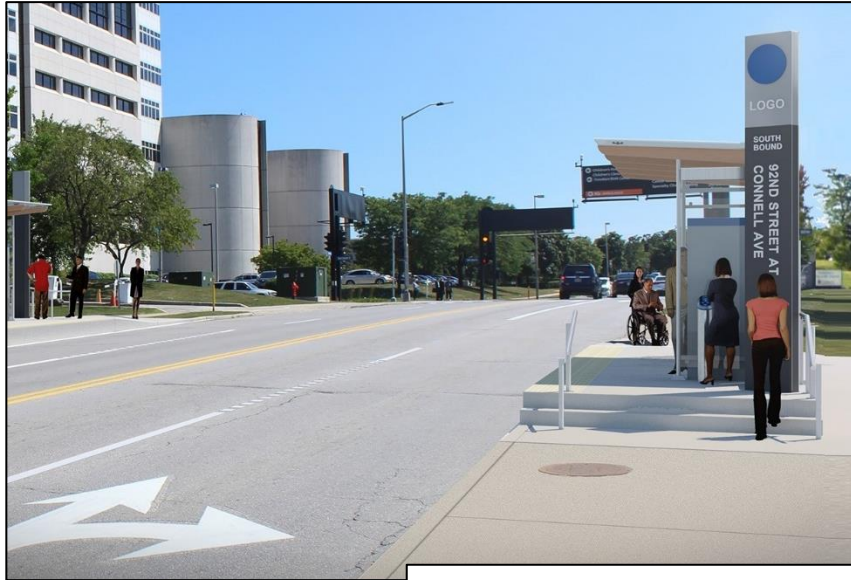

Southbound 92nd & Connell

Construction Progresses

Project Total: 33 Stations
2-Year Project

Year 1 Status:

- 18 active works sites
- 8 platforms poured & cured



CONSTRUCTION

Construction Progresses

Year 1: Through Fall 2021 (Watertown Plank – 35th 27th) *On Schedule*

- Shawn Rolland, Dist. 6: Watertown Plank – Hawley
- Eddie Cullen, Dist. 15: Glenview – 45th
- Marcelia Nicholson, Dist. 5: 45th – 27th
- Priscilla Coggs-Jones, Dist. 10: 27th



Year 2: Spring to Fall 2022 (27th 16th – Van Buren) *On Schedule*

- Marcelia Nicholson, Dist. 5 & Priscilla Coggs-Jones, Dist. 10

**Construction schedule subject to change based on weather & external factors*

In the Works

- **Fare Collection System with BRT Validators**
- **Ticket Vending Machines**
 - Award status
- **Real-Time Signage**
 - Proposals Received 10/12
- **Driver Facility & Charging Station**
 - Under Construction



Watertown Plank Driver Facility & Charging Station



For more information:
eastwestbrtmke.com

Or contact:

Brittany Bertsch – MCTS Project Manager
bbertsch@mcts.org

David Locher – MCTS Transportation Manager
dlocher@mcts.org

**EAST
WEST BRT**
