East-West Bus Rapid Transit Project Update – Milwaukee County Board



April 14, 2023

(C) ONNECT Milwaukee Co.'s East-West BRT










Stations Complete



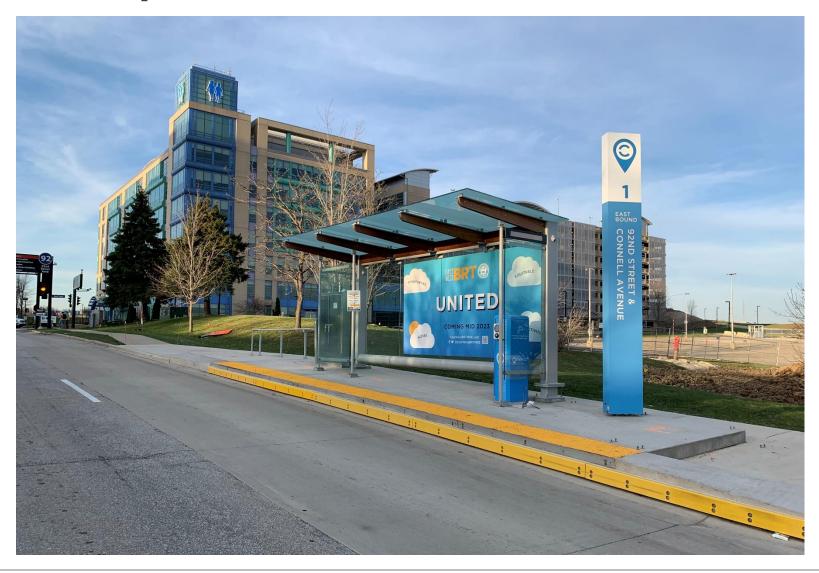

Lane Striping – April-May

Stakeholder Outreach

- County Supervisors
- Milwaukee Alders
- Story Hill
- Near West Side Partners
- Marquette University
- BID 21

Agency Coordination

Police/Fire/DPW

Public Resources

- Online
- Mailing to Residents



DEDICATED BUS LANE : HOW-TO GUIDE







Bus	Batteries/MPCS	Original Delivery	New Delivery	Status
BEB-01	Yes/Yes	11/6/22	-	DELIVERED
BEB-02	Yes /Yes	3/1/23	3/22/23	DELIVERED
BEB-03	Yes/ (Mar 2)	3/8/23	3/29/23	DELIVERED
BEB-04	Yes/(Feb 10)	3/15/23	4/12/23	DELIVERED
BEB-05	Yes / Yes	3/22/23	5/3/23	DELIVERED
BEB-06	Yes / Yes	3/29/23	5/10/23	
BEB-07	Yes / yes	4/5/23	5/24/23	
BEB-08	Partially/ (Feb 17)	4/12/23	6/8/23	
BEB-09	No / (Feb 23)	4/19/23	6/14/23	
BEB-10	No / (Feb 28)	4/26/23	6/21/23	
BEB-11	(Jan 30)/ (Mar 3)	5/3/23	7/5/23	



Order of 11 BEBs

- 7 on property by June 4
- Supply-chain: Batteries/Installation
- Mitigation:
 - Supplement BRT Line with Clean Diesels until BEBs arrive

All 11 at MCTS early July

SUBJECT TO CHANGE

Preparing for Launch

System Integration Testing

Training our Staff

- Operators, Dispatchers, Route Supervisors
- Mechanics, Maintenance

Informing the Public

- Integrated Media Campaign
- Service every 10 min.
- Downtown to Medical Center 30 min.

Pre-Revenue Operations







Service Starts Sunday, June 4

Monday, June 5

- Ribbon-Cutting EVENT
- 10am-11am
- 27th & Wisconsin

SEE YOU THERE!







Fast, Frequent, Reliable

For more information: eastwestbrtmke.com MCTS CONNECT (ridemcts.com)



Or contact:

Brittany Bertsch – Director of Project Management bbertsch@mcts.org

David Locher – MCTS Manager of Enhanced Transit dlocher@mcts.org
