

Project Update – Milwaukee County Board

February 10, 2023





Revenue Service Date June 4, 2023


- Enhanced Boarding
- Premium Shelters
- Off-Board Fare Collection
- Real-Time Signs
- Dedicated Lanes
- Battery Electric Buses (BEBs)





Adding the Amenities

- Ticket Vending Machines (TVMs)
- Real-Time Signs
- Fare Validators

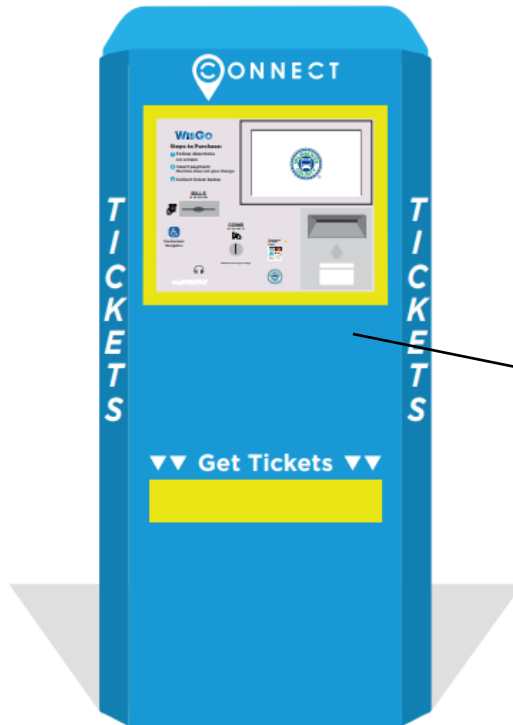



Battery Electric Buses – Delivery Delay

Bus	Batteries/MPCS	Original Delivery	New Delivery
BEB -00	Yes/Yes	11/6/22	MET
BEB -04	Yes /Yes	3/1/23	3/22/23
BEB -03	Yes/ (Mar 2)	3/8/23	3/29/23
BEB-05	Yes/(Feb 10)	3/15/23	4/12/23
BEB -02	Yes / Yes	3/22/23	5/3/23
BEB-06	Yes / Yes	3/29/23	5/10/23
BEB-01	Yes / yes	4/5/23	5/24/23
BEB-07	Partially/ (Feb 17)	4/12/23	6/8/23
BEB -08	No / (Feb 23)	4/19/23	6/14/23
BEB-09	No / (Feb 28)	4/26/23	6/21/23
BEB-10	(Jan 30)/ (Mar 3)	5/3/23	7/5/23

SUBJECT TO CHANGE

Order of 11 BEBs

- 7 on property by June 4
- Supply-chain: Batteries/Installation

All 11 at MCTS early July






Priorities

- Meeting our FTA Revenue Service Date: June 4
- Meeting our service levels
- Mitigation:
 - Supplement BRT line with 2023 clean-diesels
 - Wrap each with Ads for the BRT
 - As each BEB arrives, a wrapped clean-diesel can be used anywhere in the MCTS grid



Nova BEB

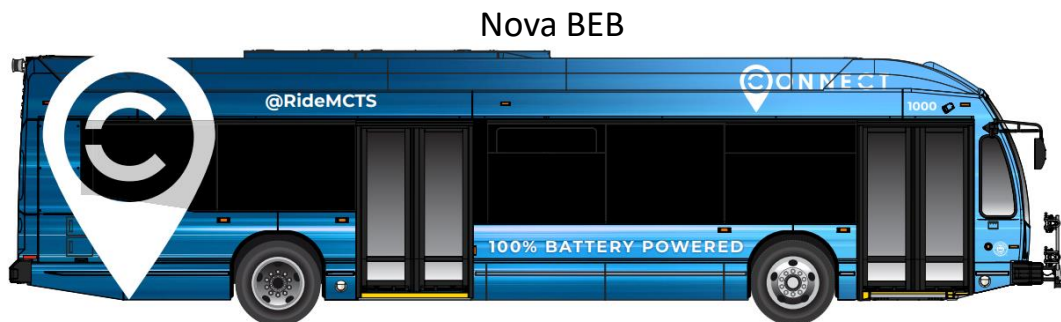

Nova BEB



Wrapped Clean-Diesel (concept)

Stop-Gap Solution

Wrapped Buses - Examples



NOTE: The views and opinions expressed in paid advertisements on MCTS buses and bus shelters are those of the advertiser and do not necessarily reflect the views and opinions of MCTS or its employees.



Stop-Gap Solution

For more information:
eastwestbrtmke.com
[MCTS CONNECT \(ridemcts.com\)](http://MCTS CONNECT (ridemcts.com))



Or contact:

Brittany Bertsch – Director of Project Management
bbertsch@mcts.org

David Locher – MCTS Manager of Enhanced Transit
dlocher@mcts.org
